

Migrate Smarter, Not Harder

SAP BusinessObjects BI → Power BI/Fabric, Tableau, Qlik Sense


4,000 REPORTS PORTFOLIO	40–60% COST REDUCTION	3 Platforms ONE TEAM	7 Milestones PAYMENT GATES
----------------------------	--------------------------	-------------------------	-------------------------------

MILESTONE PAYMENT SCHEDULE

ID	TIMING	MILESTONE	KEY DELIVERABLES
M1	Mo 2	CoP Infrastructure Established	Portal, governance charter, community cadence
M2	Mo 3	AoA Evaluation Delivered	Platform comparison, TCO analysis, briefing
M3	Mo 4	Portfolio Assessment & Roadmap	BusinessObjects inventory classified, roadmap approved
M4	Mo 6	CoP Adoption Threshold	≥30 members, ≥75% attendance, first showcase
M5	Mo 9	Pilot Migration Complete	≥150 reports accepted, self-service ≥40%
M6	Mo 14	Full-Scale Migration Checkpoint	≥75% portfolio migrated, complex complete
M7	Mo 18	Decommission & Transition	100% resolved, CoP agency-sustained

Phase 1 Mo 1–4 Phase 2 Mo 5–9 Phase 3 Mo 10+

STAFFING TIMELINE

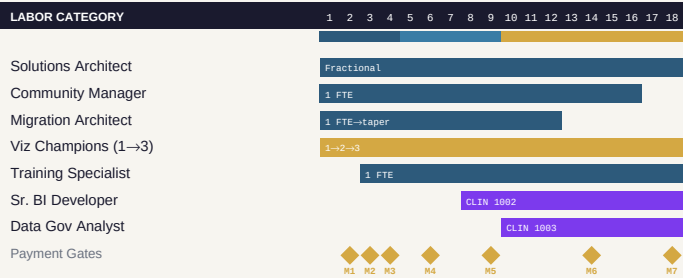

Outcome-Based Invoicing: T&M flexibility + milestone accountability. Reusable across any agency facing SAP BI platform sunset and enterprise modernization.

CLIN STRUCTURE

CLIN	TYPE	DESCRIPTION	GATES STRUCTURE
0001	BASE	CoP Enablement & Mgmt	M1, M4T&M
0002	BASE	AoA & Migration Arch	M2, M3T&M
0003	BASE	Training & Enablement	M3, M5T&M
1001	OPT	Viz Dev — Standard	M5, M6T&M+Ceil
1002	OPT	Viz Dev — Advanced	M6, M7T&M+Ceil
1003	OPT	Data Governance	M7 T&M+Ceil

THE TEAM

Solutions Architect	Sr. Data Analytics Architect	Fractional
Community Manager	Knowledge Mgmt Specialist	1 FTE
Visualization Champions	BI Developer / Data Viz Eng	2–3 FTE
Migration Architect	Sr. Enterprise BI Architect	1 FTE
Training Specialist	Technical Training Developer	1 FTE

PHASED APPROACH

- Phase 1 Mo 1–4
AoA Support & CoP Standup
Platform evaluation, BusinessObjects assessment, CoP infrastructure.
- Phase 2 Mo 5–9
Pilot Migration & Enablement
Office hours, showcases, paired development.
- Phase 3 Mo 10+
Scaled Migration & Execution
Optional CLINs activate. Self-sufficient + contractor-led.

SUCCESS METRICS

- CoP Participation**
Members, office hours, KB articles
- Self-Service Ratio**
Agency-led vs. contractor-led
- Cost per Report**
Benchmarked vs. traditional migration
- Decommission Timeline**
Tracking to full BusinessObjects exit

WHY MIGRATEIQ

- Tri-Platform Fluency**
Power BI/Fabric, Tableau, Qlik Sense — no vendor bias.
- CoP Model is Proven**
Peers teach peers; self-sustaining.
- Built-In Demand Signal**
Optional CLINs on evidence, not guesswork.
- Zero Lock-In**
All deliverables transfer to the agency.
